



REPLY TO
ATTENTION OF:

DEPARTMENT OF THE ARMY
INSTALLATION MANAGEMENT COMMAND
HEADQUARTERS, U.S. ARMY GARRISON, ALASKA
1060 GAFFNEY ROAD #6000
FORT WAINWRIGHT, ALASKA 99703-6000

23 February 2012

IMFW-PWE

Ms. Deb Caillouet
Alaska Department of Environmental Conservation
Division of Spill Response and Contaminated Sites Program
555 Cordova Street
Anchorage, AK 99501

Subject: Revisions to the Negotiated Schedule for Primary and Secondary Documents for: Operable Unit 6, Former Communications Site, aka Taku Gardens, Fort Wainwright, Alaska.

Dear Ms. Caillouet,

On 28 March 2011, in compliance with Paragraph 6 of the Amendment to Federal Facility Agreement Under CERCLA Section 120, Administrative Docket Number: 1092-04-10-120 dated February 2007, the Remedial Project Managers developed and submitted a timetable for scheduling the activities for Operable Unit 6 – Former Communications Site. Recent events require the schedule be amended.

Extensive revisions and clarifications were requested by the US Environmental Protection Agency Region 10 policy personnel during the November 17, 2011 Proposed Plan Review Meeting. A schedule revision is required to provide sufficient time to incorporate the accepted changes. The Army requests concurrence with the attached revised schedule for Operable Unit 6 – Former Communications Site.

During discussions on February 2, 2012 the Remedial Project Managers developed a revised schedule for the required documents. The Army has since extended the schedule to provide Agencies with extended review/comment periods as shown on the attached schedule (Encl #2) for completing reviews of the Proposed Plan and Record of Decision as required by the Fort Wainwright Federal Facilities Agreement as amended. The Remedial Project Managers signature on the attached memorandum (Encl #1) will formally document all parties' approval of this schedule revision for the Administrative Record.

If you have additional questions or concerns regarding this action, please contact the undersigned, Mr. Joseph Malen at the Public Works Environmental Office by calling 907-361-4512 or by emailing joseph.s.malen.civ@mail.mil. Thank you for your continued support in this matter.

JOSEPH S. MALEN
Remedial Project Manager
Fort Wainwright, Alaska

- 2 Encl
1. Memorandum for the
Administrative Record
2. Gantt Chart by Jacobs Engineering

CF:
U.S. Army Installation Management Command, Pacific
U.S. Army Environmental Command, Ft. Sam Houston, TX
HQ, U.S. Army Garrison Fort Wainwright CERCLA Administrative Record

23 February 2012

MEMORANDUM FOR: The Fort Wainwright Alaska Comprehensive Environmental Response, Compensation, and Liability Act (CERCLA), Administrative Record for Operable Unit 6, Former Communications Site, aka Taku Gardens.

SUBJECT: Revised Schedule for Primary and Secondary Documents for: Operable Unit 6, Former Communications Site, Fort Wainwright, Alaska.

The undersigned acknowledge approval and acceptance of the attached revised timetable for scheduling the activities for Operable Unit 6 – Former Communications Site, aka Taku Gardens as required by the Fort Wainwright Federal Facility Agreement as amended.

Primary Documents

Feasibility Study
Record of Decision

Completion Date

May 13, 2011
January 11, 2013

Secondary Documents

Proposed Plan

Completion Date

June 23, 2012



Joseph S. Malen
Remedial Project Manager
US Army Garrison, Fort Wainwright
Fort Wainwright, Alaska

23 Feb 12

Date

Jacques Gusmano
Remedial Project Manager
US Environmental Protection Agency
Region 10 – Office of Environmental Clean-up
Anchorage, Alaska


Date

Deb Caillouet
Remedial Project Manager
Alaska Department of Environmental Conservation
Division of Spill Response and Contaminated Sites Program
Anchorage, Alaska

Date

ENCL # 1

Activity ID	Activity Description	Rem Dur	Early Start	Early Finish
Taku Operable Unit 6				
Post RI Action Memorandum				
2011 Ground Water Data Report				
GWM2011	Prepare Draft Report	28	31JAN12	27FEB12
GWM2021	Review Draft Report	14	28FEB12	12MAR12
GWM2031	Prepare/Submit final Report	14	13MAR12	26MAR12
FCS Ground Water Summary Report				
2010 Field Activities Report				
FAR2011	Prepare Pre-Draft Report	174	09SEP11	29FEB12
FAR2021	Review Pre-Draft Report	7	01MAR12	07MAR12
FAR2031	Prepare Draft Report	7	08MAR12	14MAR12
FAR2041	Review Draft Report	14	15MAR12	28MAR12
FAR2051	Prepare/Submit final Report	14	29MAR12	11APR12
Post RI Action Memorandum				
PRAM12	Prepare pre-draft RI Action Memorandum	11	22MAR12*	01APR12
PRAM13	Review of pre-draft RI Action Memorandum	7	02APR12	08APR12
PRAM14	Prepare draft RI Action Memorandum	7	09APR12	15APR12
PRAM15	Review of draft RI Action Memorandum	14	16APR12	29APR12
PRAM16	Prepare/Submit final RI Action Memorandum	14	30APR12	13MAY12
Proposed Plan				
P31	RPMs review draft Rev. 1 PP (EPA Meeting)	20	17NOV11	06DEC11

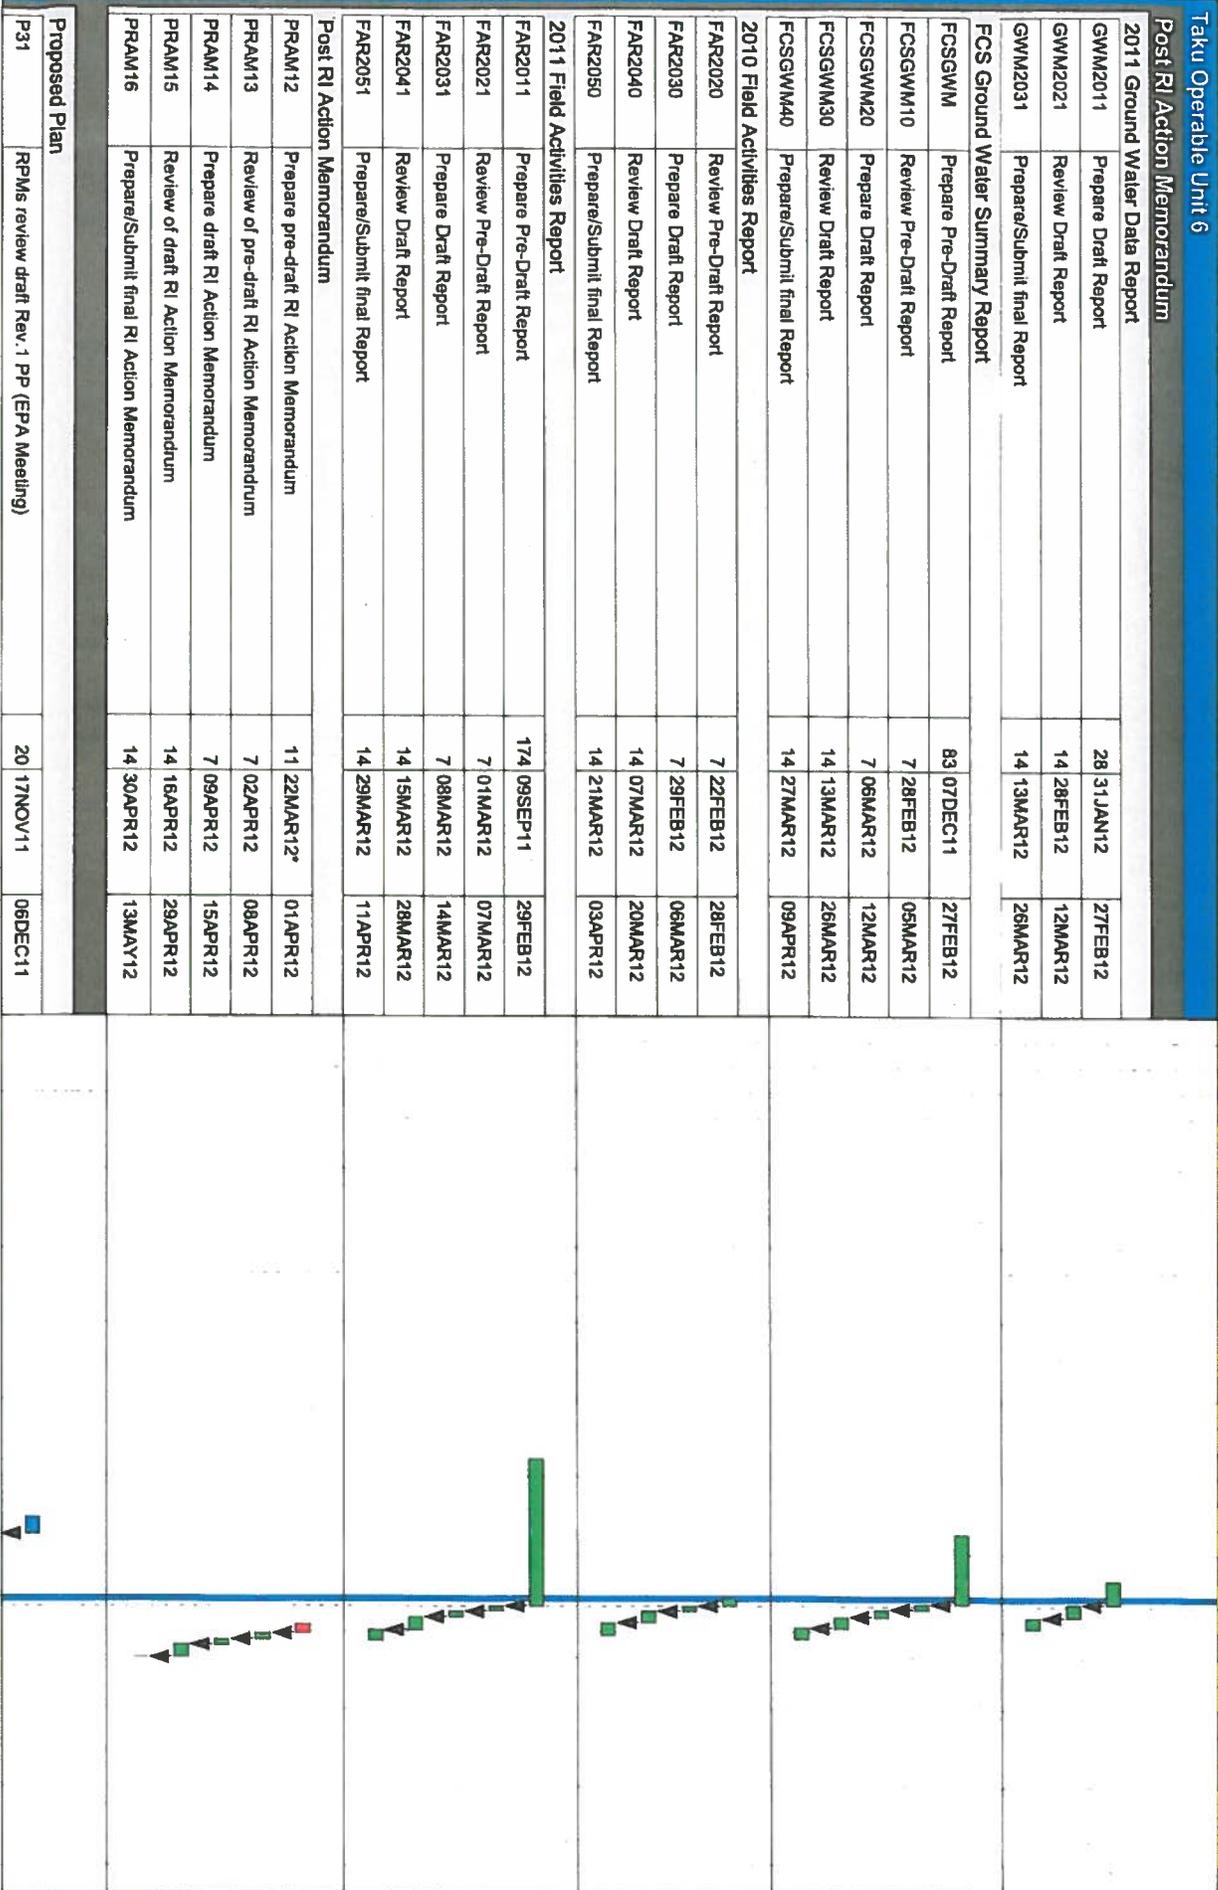

Start Date: 22APR10
 Must Finish Date: 22FEB12
 Data Date: 23FEB12 15:17
 Run Date: 23FEB12 15:17


TAKU Operable Unit 6

Sheet 1 of 2



© Primavera Systems, Inc.

Activity ID	Activity Description	Rem Dur	Early Start	Early Finish
P310	Jacobs Prepares RTCs	62	07DEC11	06FEB12
P320	RPMs Review RTCs	14	07FEB12	20FEB12
P330	Jacobs Prepares Pre-Final PP	26	22FEB12	18MAR12
P340	Army Reviews Pre-Final PP	14	19MAR12	01APR12
P350	Jacobs Prepares Final PP	14	02APR12	15APR12
P51	RPM approve/review PP	14	16APR12	29APR12
P61	Public notice of PP period	45	30APR12	14MAY12
P71	Public comment period	33	15MAY12	16JUN12
P81	Public meeting	1	17JUN12	17JUN12
P91	Incorporate public comments	7	18JUN12	24JUN12
Record of Decision				
D1	Jacobs prepares pre-draft ROD	324	18JUN11	06MAY12
D21	Army Reviews pre-draft ROD	26	07MAY12	01JUN12
D31	Jacobs prepares draft ROD	27	02JUN12	28JUN12
D41	RPMs review draft ROD	55	29JUN12	22AUG12
D51	Jacobs prepares RTCs	14	23AUG12	05SEP12
D61	RPMs review RTCs	14	06SEP12	19SEP12
D91	Jacobs prepares draft ROD	31	20SEP12	20OCT12
D911	Army Reviews draft ROD	14	21OCT12	03NOV12
D961	Jacobs prepares final ROD	14	04NOV12	17NOV12
D971	ROD is submitted for final signature	55	18NOV12	11JAN13
D981	ROD is Signed	1	11JAN13	11JAN13

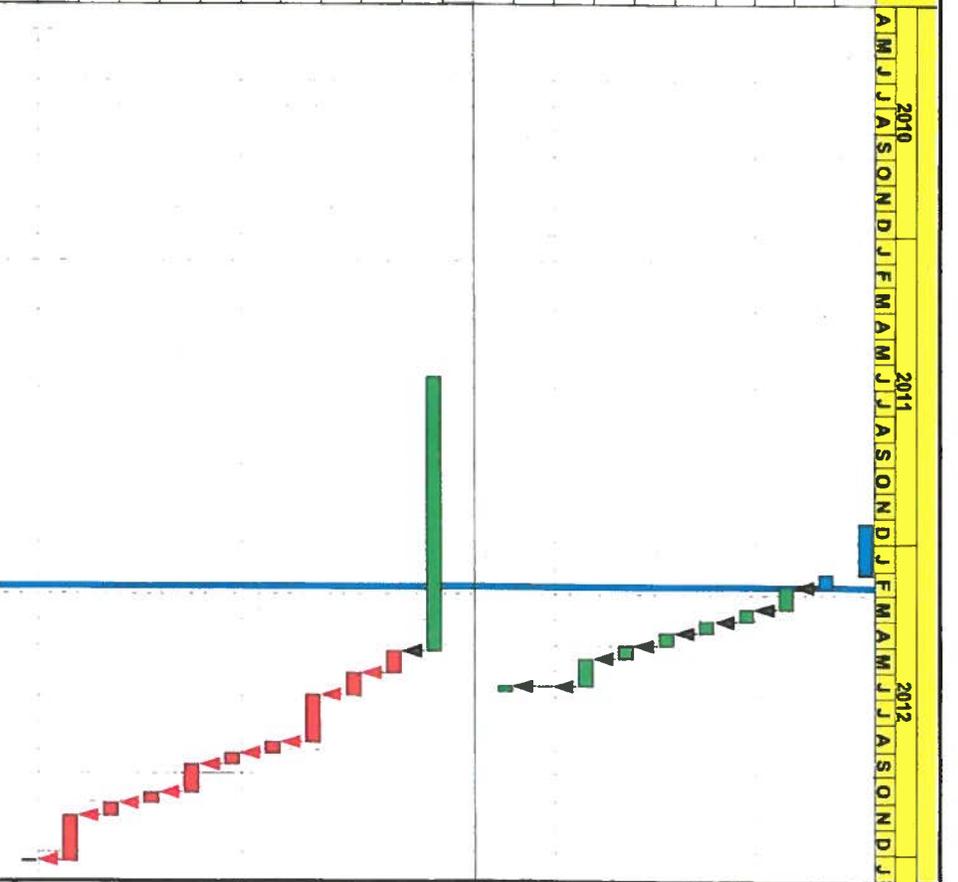

Start Date
Must Finish Date
Data Date
Run Date

22APR10
22FEB12
23FEB12 15:17

TAKU
Taku Operable Unit 6

Sheet 2 of 2

© Primavera Systems, Inc.



23 February 2012

MEMORANDUM FOR: The Fort Wainwright Alaska Comprehensive Environmental Response, Compensation, and Liability Act (CERCLA), Administrative Record for Operable Unit 6, Former Communications Site, aka Taku Gardens.

SUBJECT: Revised Schedule for Primary and Secondary Documents for: Operable Unit 6, Former Communications Site, Fort Wainwright, Alaska.

The undersigned acknowledge approval and acceptance of the attached revised timetable for scheduling the activities for Operable Unit 6 – Former Communications Site, aka Taku Gardens as required by the Fort Wainwright Federal Facility Agreement as amended.

Primary Documents

Feasibility Study
Record of Decision

Completion Date

May 13, 2011
January 11, 2013

Secondary Documents

Proposed Plan

Completion Date

June 23, 2012




Joseph S. Malen
Remedial Project Manager
US Army Garrison, Fort Wainwright
Fort Wainwright, Alaska




Date

Jacques Gusmano
Remedial Project Manager
US Environmental Protection Agency
Region 10 – Office of Environmental Clean-up
Anchorage, Alaska

Date



Deb Caillouet
Remedial Project Manager
Alaska Department of Environmental Conservation
Division of Spill Response and Contaminated Sites Program
Anchorage, Alaska



Date

ENCL # 1
